



Oxford Station Enhancements Project

July 2026 update

Who we have presenting



Tim Walden

Capital Delivery Director



Giles Clark

Project Director -
Enhancements



Matt Riddick

Project Director

Botley Road update

South walkway
opened on time in
July 2026



Highway Opening
delayed 4-6 weeks



North walkway
opened on time in
August 2025



Botley Road will reopen up to 6 weeks later than planned, a firm date will be confirmed by Wednesday 29th July.

We want to take this opportunity to say sorry for this further delay, to explain the reason for the delay and to talk to you about what we are doing about it.

- Work to replace a gas main beneath Botley Road has been identified as urgently needing to be completed before the road can reopen to traffic.
- SGN will replace a metal pipe with a plastic one. This will ensure they can avoid disruptive gas leaks in the future and continue to maintain a safe and efficient gas supply.
- We are working closely with SGN to minimise the impact of this additional work. At this time we are being realistic with the additional time needed to complete this work.
- Due to the location of the gas main, it is not possible to undertake all this work at the same time to completing the work to the road.

Route to Road Re-Opening

South walkway
opened on time in
July 2026


✓

Highway Opening
delayed 4-6 weeks

✗

North walkway
opened on time in
August 2025

✗

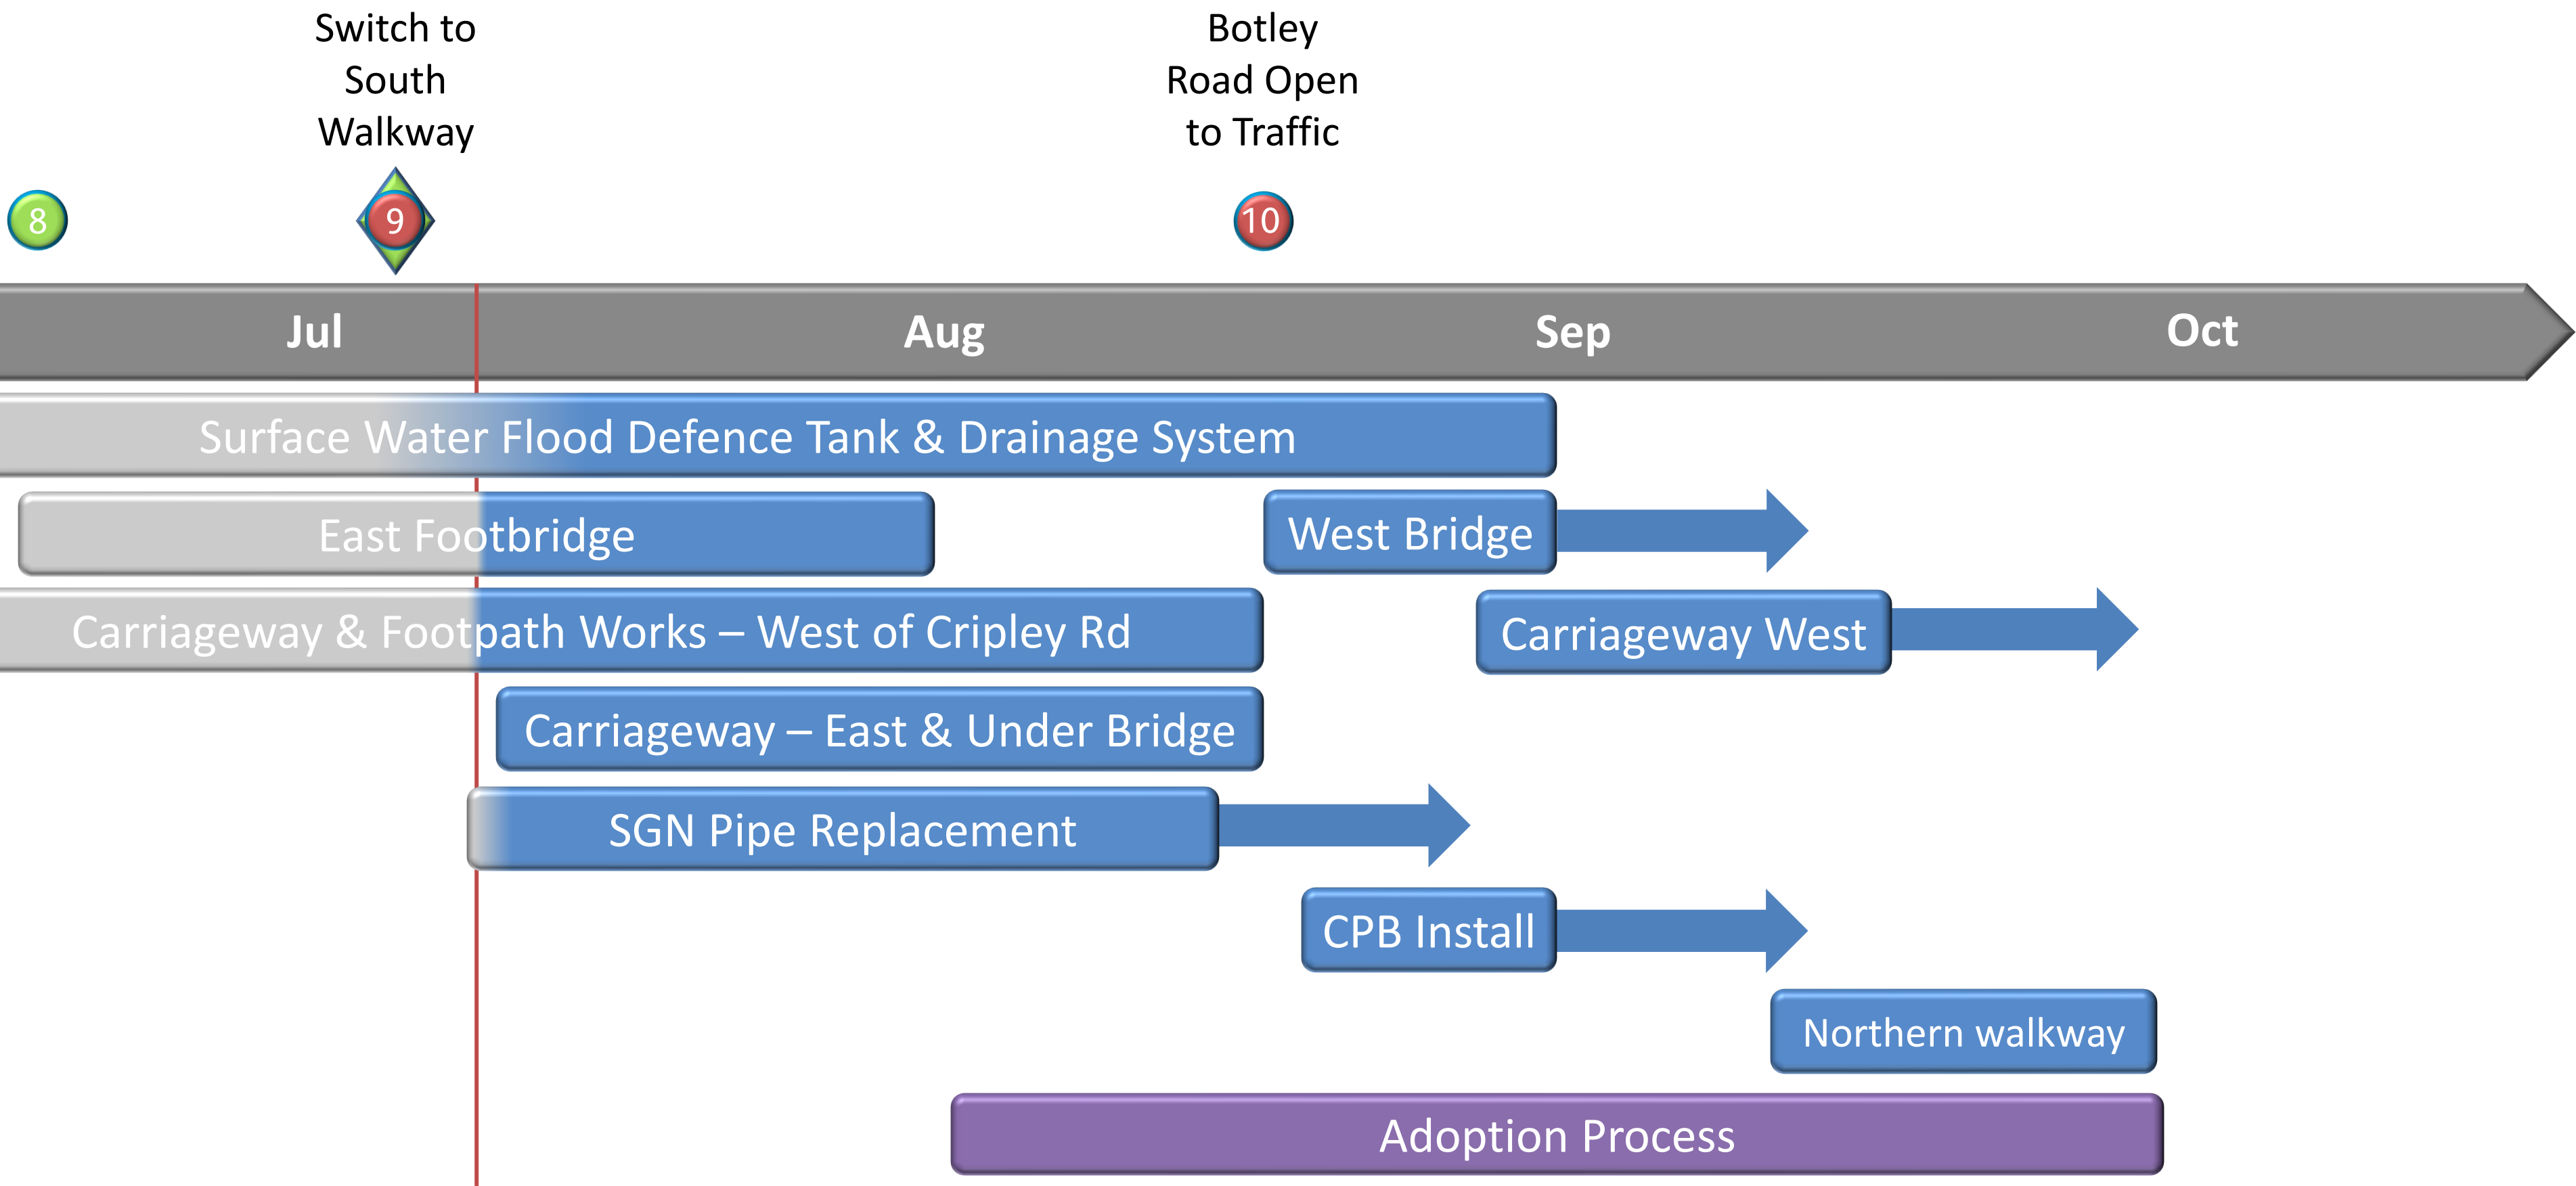


6 weeks for SGN to replace and commission

- Section 1 – 35m
- Section 2 – 7m
- Section 3 – 22m
- Commissioning

existing plastic gas main

existing cast iron gas main

new plastic gas main

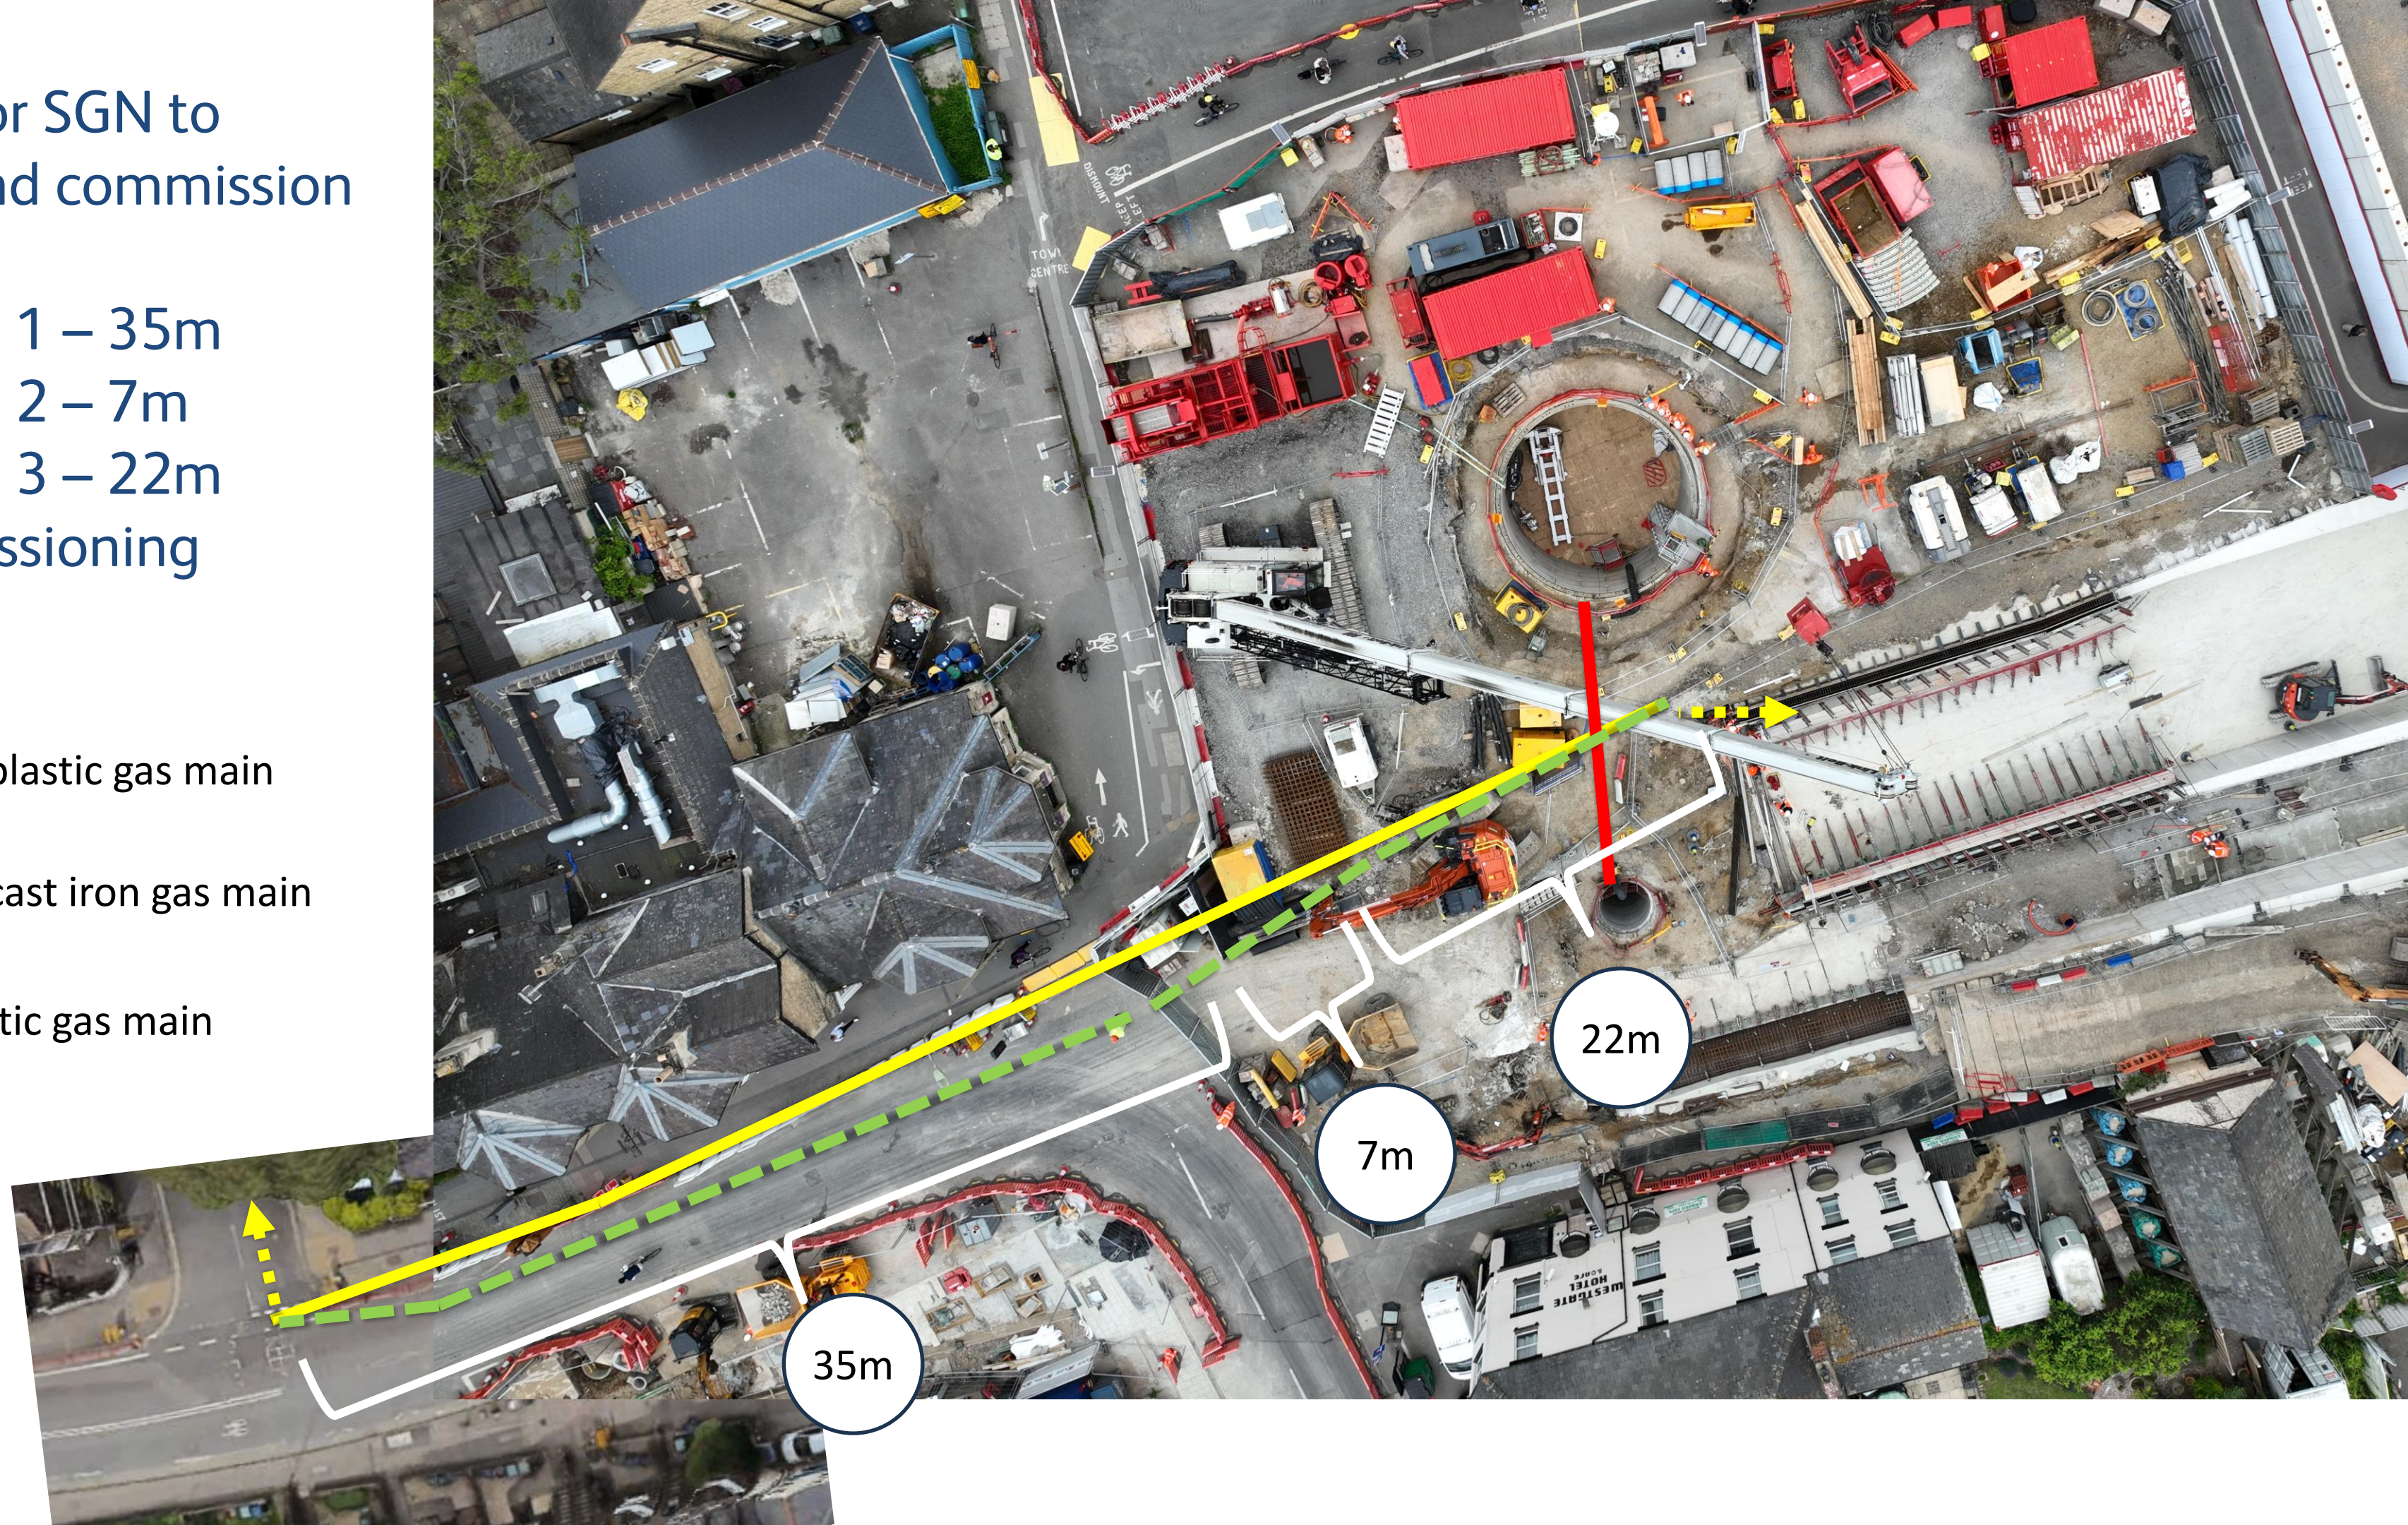

Next resident meeting



Date	Time	Venue
Wednesday 19 August 2026	17:00 – 18:00	The King's Centre Osney Mead, Oxford OX2 0ES

Future meeting dates to be confirmed

OxfordFeedback@networkrail.co.uk
