


Oxfordshire Connect Newsletter

1 July 2026



Oxford Station Enhancements Project



	Key projects	Date	Status
①	Foundations for bridge supports on station side completed	17-Mar-25	Complete
②	700mm clean water pipe completed (Thames Water)	30-May-25	Complete
③	125mm clean water pipe completed (Thames Water)	31-Jul-25	Complete
④	Sewer diversion completed	27-Aug-25	Complete
⑤	Northern pedestrian way available for public use	31-Aug-25	Complete
⑥	Southern pedestrian/cycleway works to start	30-Nov-25	Complete
⑦	Botley Road bridge replacement completed	9-Feb-26	Complete
⑧	New ground water flood defence concrete structure completed	30-June-26	Complete
⑨	New surface water flood defence tank completed	17-Jul-26	Re-sequenced*
⑩	Botley Road reopened to traffic	31-Aug-26	

*Milestone 9 re-sequenced to 17 July due to an alternative drainage solution that removes build complexity and stakeholder disruption.

The resequencing of milestone 9 does not impact the road opening date.

Resident meeting

Wednesday 1 July, 5-6PM

West Oxford Community Centre

Resident meeting - 1 July

A reminder that the resident meeting will take place today (**Wednesday 1 July**) from **5-6PM at West Oxford Community Centre**.

This was rearranged following last week's extreme temperatures. Come along to meet the project team, find out the latest information and ask any questions. If you can't join us, we share the presentation on our [website](#) after each meeting.

Ground water flood defence structure completed

The 120-metre groundwater flood defence structure is now complete, including waterproofing, steel reinforcement and concrete pours. This is milestone 8 in the table above and a key part of flood prevention measures.



Pictured above: new ground water flood defence structure completed.

Footway and kerb replacement works

Work to replace and realign footways and kerb lines continues, in preparation for the reopening of Botley Road in August. This work has taken longer than expected due to utility services in the footway that had not been installed to the standard depth and blocked drains.

The work currently taking place, between the River Hotel and the junction of Botley Road with Mill Street, is due to be completed this week (week beginning 29 June). Work is also taking place within our site compound (second stage in the map shown below) near to the Westgate Hotel.

The next stage of this work will move to the north side of Botley Road, including the junction with Abbey Road.

This work will be carried out in stages, to minimise disruption as much as possible, and is due to be completed in August.

This work includes:


- Temporarily removing, then realigning and replacing footpaths
- Realigning and installing kerbs
- Laying ducting for street lighting
- Removing some of the existing footway tarmac
- Retarmacking and laying paving stones

Access for residents, pedestrians, cyclists and vehicles will be maintained at all times.

To allow this work to take place safely:

- Sections of footpath will be closed off temporarily, with an alternative route on the other side of the road.
- Marshals will be on hand to support and to provide continued access to properties.
- Traffic management will be in place, with one half of each section of road coned off in stages.
- There will be some temporary changes to walking routes, crossing points, bike waiting areas at traffic lights, and points where cyclists will need to dismount. These will be signposted and marshals will be on hand to support.

We will share the latest information about this work on [Facebook](#) and on our [website](#). For any questions, please contact: **OxfordFeedback@networkrail.co.uk**

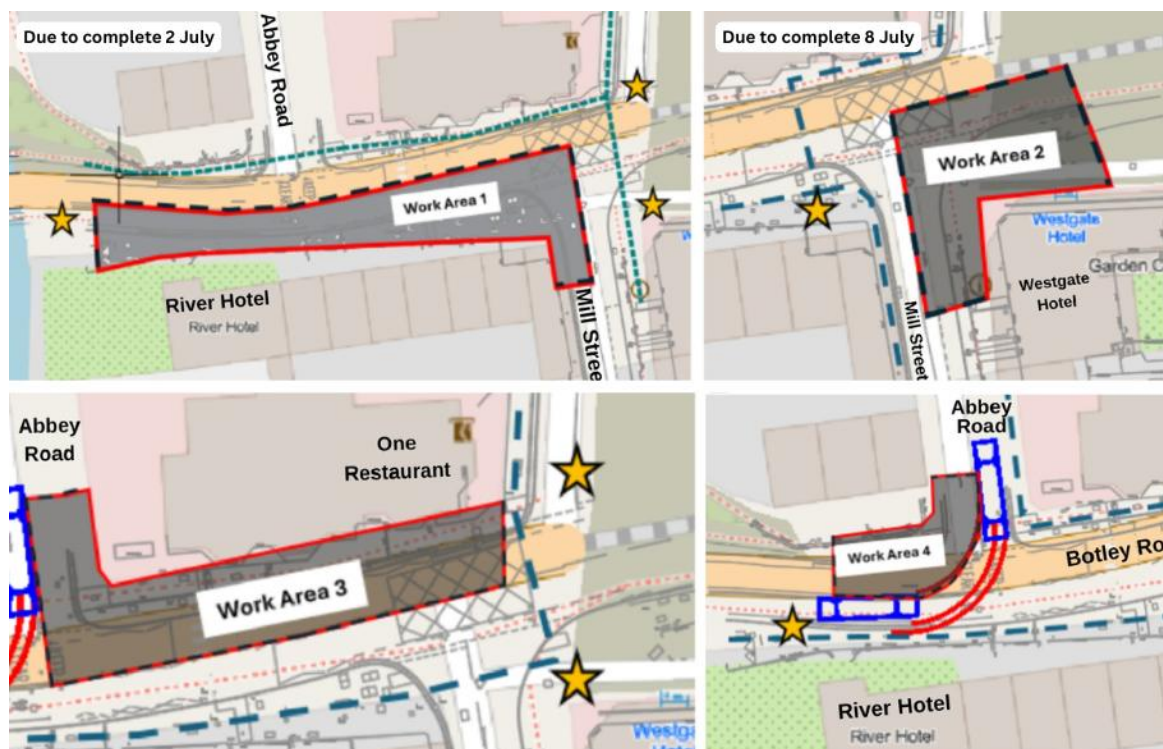

Pictured above: maps showing locations of the first stage (top left); second stage (top right); third stage (bottom left) and fourth stage (bottom right) of the footway and kerb realignment works.

Southern walkway

The southern walkway is taking shape, with paving slabs laid and concrete cladding being fixed to the wall. The southern walkway will open this month, when the northern walkway will temporarily close so that finishing works can be carried out.



Pictured above: (left) new footway tarmac on Botley Road, near the River Hotel; (middle) newly installed paving slabs on the southern walkway; (right) concrete cladding on the southern walkway walls.

Surface water drainage system

Tunnelling works have started, to connect the new surface water storage tank with the existing Thames Water system to carry rainwater from Botley Road.




Pictured above: the tunnel boring machine (TBM) in the 12-metre-deep water storage tank shaft.

Bike parking - temporary changes

The top two rows of uncovered bike racks at Oxford station are temporarily out of use while work on the new footbridge takes place. This is essential to allow these works to be carried out safely.

The footbridge works are expected to take up to six weeks. We will work to return access to the bike parking as soon as it is safe to do so.

The 12 bike racks under the shelters and nearest to Park End Street are not affected and will remain available for use.

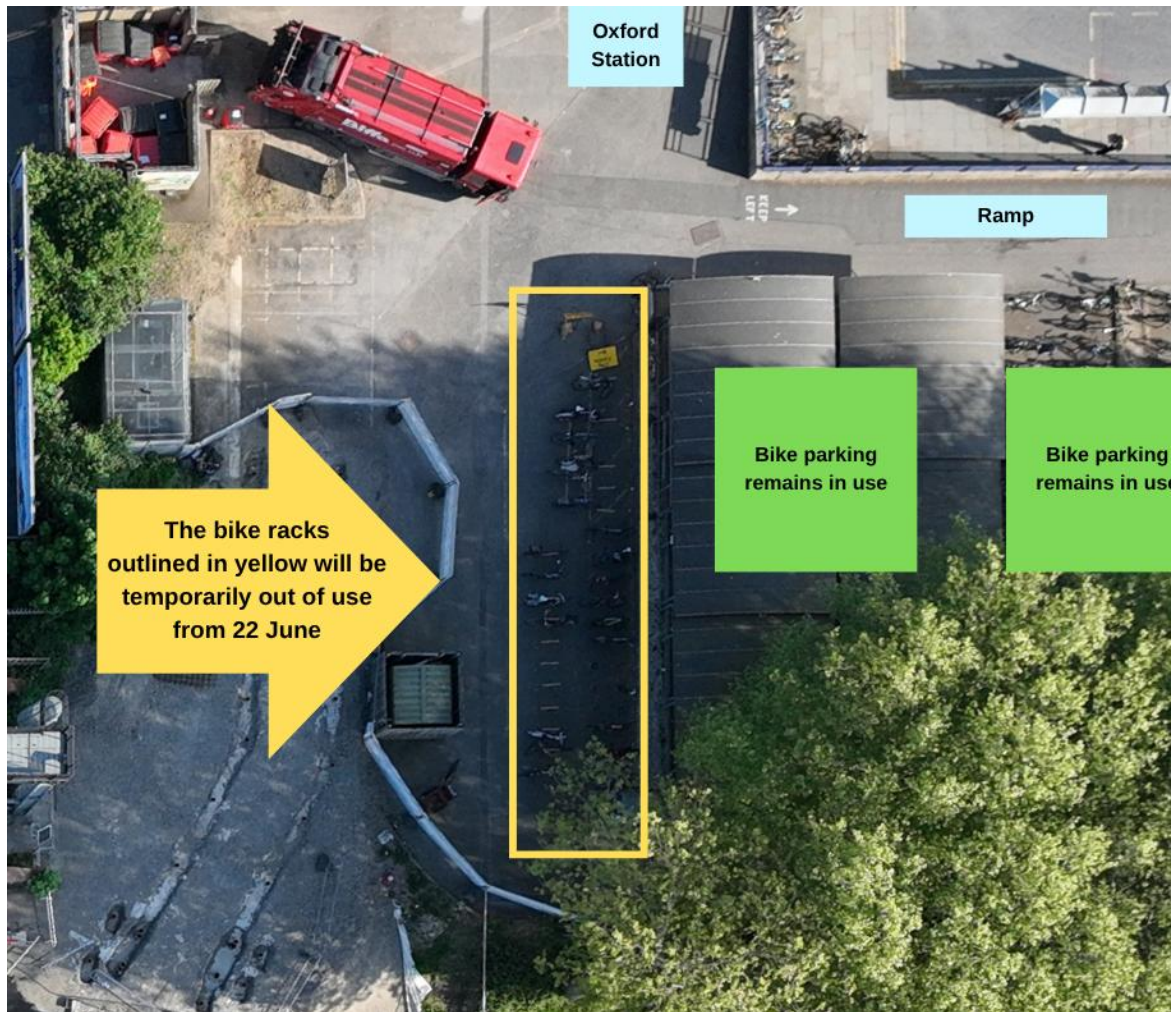

Pictured above: aerial view of the bike parking at Oxford station.



Sign up to our digital notification system to keep informed about works near you.

You can now stay informed with Network Rail's free digital notification service. By signing up, you'll receive direct updates about:

- Upcoming planned railway works in your area
- Updates or changes to scheduled works
- Urgent works
- Important project news that could affect you, including Oxfordshire Connect

Sign up link: <https://lineside.networkrail.co.uk/oxfordshireconnect>

Resident meetings

Come along to meet the project team, find out the latest information and ask any questions. If you can't join us, we share the presentation on our [website](#).

Date	Time	Venue
Wednesday 1 July 2026	17:00 - 18:00	West Oxford Community Centre, Botley Road, Oxford OX2 0BT
Wednesday 22 July 2026	17:00 - 18:00	West Oxford Community Centre, Botley Road, Oxford OX2 0BT
Wednesday 19 August 2026	17:00 - 18:00	West Oxford Community Centre, Botley Road, Oxford OX2 0BT

Business meeting

Date	Time	Venue
Wednesday 22 July 2026	18:30 - 19:30	West Oxford Community Centre, Botley Road, Oxford OX2 0BT

Further information:

Web: networkrail.co.uk/OxfordshireConnect

Facebook: facebook.com/oxfordshireconnect

Email: OxfordFeedback@networkrail.co.uk

Phone: 03457 11 41 41 (24-hour national helpline)

Help for people to get to the city centre

The Botley Flyer provides a free service to help people get into the city centre. On bank holidays, the Botley Flyer runs on the Sunday timetable.

BOTLEYFLYER

FREE accessible transport from Botley Road to Oxford City Centre

Monday - Saturday

West Oxford Community Centre pick-up 10am, 12pm, 3pm
Magenta self-storage bus stop pick-up 10.05am, 12.05pm, 3.05pm
Elms Parade West Way bus stop pick-up 10.10am, 12.10pm, 3.10pm

City Centre return journeys starting at 11am, 1pm, 4pm

Sunday

West Oxford Community Centre pick-up 9.30am
Magenta self-storage bus stop pick-up 9.35am
Elms Parade West Way bus stop pick-up 9.40am

City Centre return journeys starting at 12.30pm

For all journeys, the driver will make arrangements with passengers for return journeys before dropping them off

01865 768 329 to book a wheelchair space

OxfordFeedback@networkrail.co.uk for more information

NetworkRail


SUMMERTOWN - JERICHO - BEAUMONT STREET - WESTGATE CENTRE



OXFORD
CITY
COUNCIL

THE FREE
OXFORD APP





SHOP

EAT

DO

Discover



Search
'Discover App'
In your google play or app store



Explore Oxford with the Discover App

The Discover app is ready and waiting to be your guide around Oxford City Centre. Find places to shop, eat and things to do throughout the city to suit all tastes.

Download today for free!



If you have any questions about the improvement work in and around the station, then please do feel free to contact us by clicking the logo to the left, calling us on **03457 11 41 41**, or emailing: OxfordFeedback@networkrail.co.uk
